Reference to last Measurement 8

M.A.R. 57 (Rule 116)

Measurement Book No. A/10 3151

Serial No..... Bill no:1- 1st and final.

Name of work.....From.....To.....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date 1	Full description, etc, of work 2	Dimensions Number 3	Length 4	Breadth 5	Depth 6	Contents 7	Reference to last Measurement 8
	Name of work:- Providing Chainlink fencing and other works towards Jakkur Aerodrum (towards western side) Gkvk Layout ward no. 07.						
	Job number:- 007-14-000100., Est. cost:- 20.00 lakhs.						
	Agreement no:- GE(P)/PR/Y2/Ag no/28/13-14 Dt:- 4th.03.2014.						
	work order no:- GE(P)/Y2/WO/28/2013-14 Dt:- 4.03.2014.						
	Agency:- Technical manager (cont) KRIDL, Bangalore.						

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
		1x1	20.20	0.60	$\frac{0.90+0.6}{2}$	9.09	
		1	20.00	0.60	$\frac{0.9+0.60}{2}$	9.00	
		1	1.60	0.60	$\frac{0.60+0.15}{2}$	0.72	
						89.12 cum.	
	Deduct for Portions	1 x 106	~~60.40~~	0.35	0.60	8.90 cum (–)	
						80.22 cum.	
	Limited to	80.05 cum @	Rs. 4227.12 per cum =			338380.96	
6)	Providing ruled pointing to coursed stone masonry with Cement Mortar 1:3 20mm deep after raking joints in depth of 20mm nicely lining, including cost of materials, labour, curing complete as per the specifications. (P. 122, I. no. 15.3						
	Compound wall pointing.						
	N. Side	1x2	30.10	—	0.80	48.10 Sqm.	
	— " —	1x2	30.10	—	0.70	42.00 Sqm.	
	— " —	1x2	12.90	—	0.65	10.77 Sqm.	
						16.77	

Executive Engineer
Project Division
Yelahanka Zone
Bangalore

Serial No..
Name of w
Name of C
Date of co

Date	F
1	

7	Reference to last Measurement 8
0.68	
1.54 Cum.	
Cum = 100311.21/-	
acle out of	
d lengths	
chg MS	
dng cut &	
hever necessary	
lead upto	
charge of the	
approved	
ansit	
te)	

M.A.R. 57 (Rule 116)

Measurement Book No. A/10 3159

Serial No.....

Name of work.....From.....To.....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date 1	Full description, etc, of work 2	Dimensions Number 3	Length 4	Breadth 5	Depth 6	Contents 7	Reference to last Measurement 8
	For Chain link fencing	1 X 106	2.30	—	—	243.80 mt	
	For gate	1 X 2	2.35	—	—	4.70 mt	
		limited to 248.40 mt.				248.50 mt.	
		248.40 mt @ 1098.36/- per mt				= 272832.62	
	9) Providing and fixing MS black pipe of 38mm dia of heavy gauge of 14 including removing the barbed wires						

Executive Engineer
Project Division
Yelahanka Zone
Bangalore

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8	
	the pipe and hang pipe between the two vertical pipe (MS Rectangular poles) and Spot welding and Chain link with MS Blank pipe including cost of all makeup wastage in cutting and scaffolding wherever necessary with all lead and lift as directed by the Engineer in charge if not etc complete including two coats of approved quality paint over one coat of shop paint (Item no - 37.4 page no 270)						
	N. Side -	1 x 3	72.50	—	—	217.50 mt.	
	W. Side (Top Bare)	3	37.10	—	—	111.00 mt.	
	S. Side	1 x 3	7.30	—	—	21.90 mt.	
		3	83.10	—	—	249.00 mt.	
						599.40 mt	
						@ 299.16 = 179316.50	

Executive Engineer
Project Division
Yelahanka Zone
Bangalore

Serial No.....
Name of work.....
Name of Contrac
Date of commen

Date	Full desc
1	
18)	Provi prepa with weld as s lead in u one c

Contents 7	Reference to last Measurement 8
like MS	
Item of	
take work,	
unloading	
lete	
.40 Agmt	
gmt = 24570=00/-	
, drawing	
of mules.	

M.A.R. 57 (Rule 116)

Measurement Book

No. A/10 3162

Serial No.....

Name of work.....From.....To.....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date 1	Full description, etc, of work 2	Dimensions				Contents 7	Reference to last Measurement 8
		Number 3	Length 4	Breadth 5	Depth 6		
		1X1	-	-	-	1 Nos	
	Item Erected & Installed					@ 4800/per No =	4800/-
	Item 31 to 31b Checked & Found						1815816.59
	Asst. Executive Engineer Project Division Yelahanka Zone Bangalore						1815816.66
						KKBDL Charges =	90801.22/-
						VAT charges =	90801.22/-
	Rupees Nineteen lakhs ninty seven Six hundred Twenty Six point Seven Seven only/-						1997626.77/-
							1997398.25
							1/9/2014

Name:- PROVIDING CHAINLINK FENCING AND OTHER WORKS TOWARD'S JAKKUR AERODRUM (TOWARD'S WESTERN SIDE) AT G.K.V.K LAY-OUT WN: 0.7

G.K.V.K. LAY-OUT PARK IN NO.07

BALAMURI TEMPLE AND OPP TO BALAMURI TEMPLE

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8

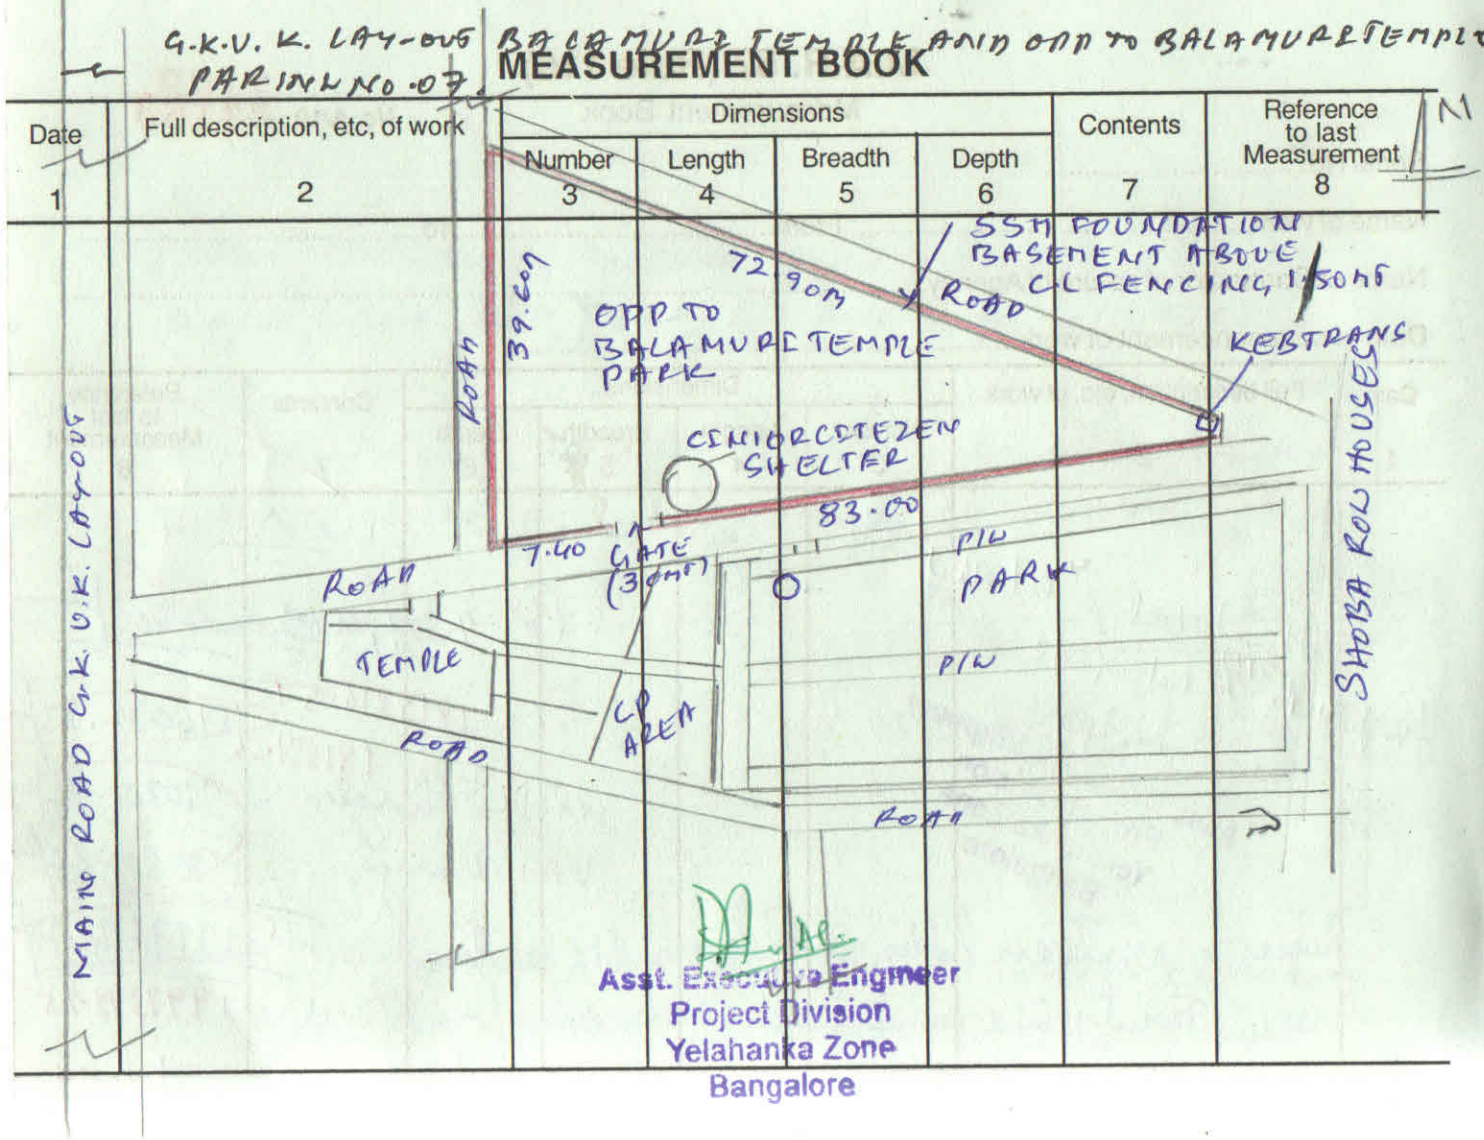

Asst. Executive Engineer
Project Division
Yelahanka Zone
Bangalore

BRN

Serial No.....

Name of work....

Name of Contrac

Date of commen

Date	Full des
1	

Audited & Admitt
Minutes la
Chetnad d
Rs 1688
and Rs. 3093

Accts. Supdt.
Project Division
B.B.M.P.

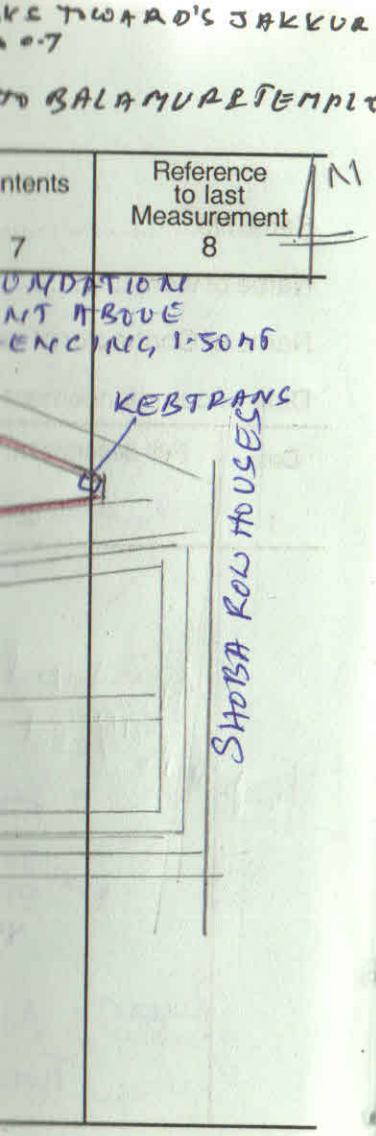

BR No. 39/14-15 dt 2/9/2014

M.A.R. 57 (Rule 116)

Measurement Book

/10 3163

Serial No.....

Name of work.....From.....To.....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
				Bill Amount		1997398	
					IT 2%	39948-	
					VAT 4%	79896-	
					F-SD 2.5%	149805-	
					L-cess 1%	19974-	
					S.R	17746-	
					CBT-0.1	1997-	
				Total Deductions		309366-	
				By cheque		1688032-	

Audited & Admitted for Rs. 1997398-

Nineteen lakhs ninety seven thousand three hundred ninety eight

Rs. 1688032- by Cheque

and Rs. 309366- by Adjustment

Accts. Supdt.
Project Division
B.B.M.P.

Exe. Engineer
Project Division
B.B.M.P.
